

Monthly Progress Update

January 2019

Jobs for

1,100

workers



Energy for

1,000,000

homes



Steps for Safety



Safety Statistics (Job to Date)

	Generation Station	Transmission Line
Near Misses	45	5
First Aids	112	6
Recordables	8	1
Lost Time	0	0
Hours Worked	1,659,646	161,620

Cricket Valley Energy Center Construction Progress



Community Outreach



The CVEC team raised just over \$10,000 this year to grant wishes to 11 families with a total of 28 children from this year's Adopt-A-Family Giving Tree. We bought, wrapped, and delivered toys, clothing, and food for these local families in time for Christmas. The team also purchased supplies for the Center of Compassion's annual drive to deliver holiday meals throughout the community.



Construction Highlights - Another Milestone



In December, the last fan deck was secured into its final position at elevation. The first fan deck was secured in June, and less than six months later, we had installed all 1900 tons of steel, and closed out this scope!

December Crew of the Month – B&W Iron Workers



May 2018




Dec 2018

Construction Progress



Progress continues on the 3 HRSG Units

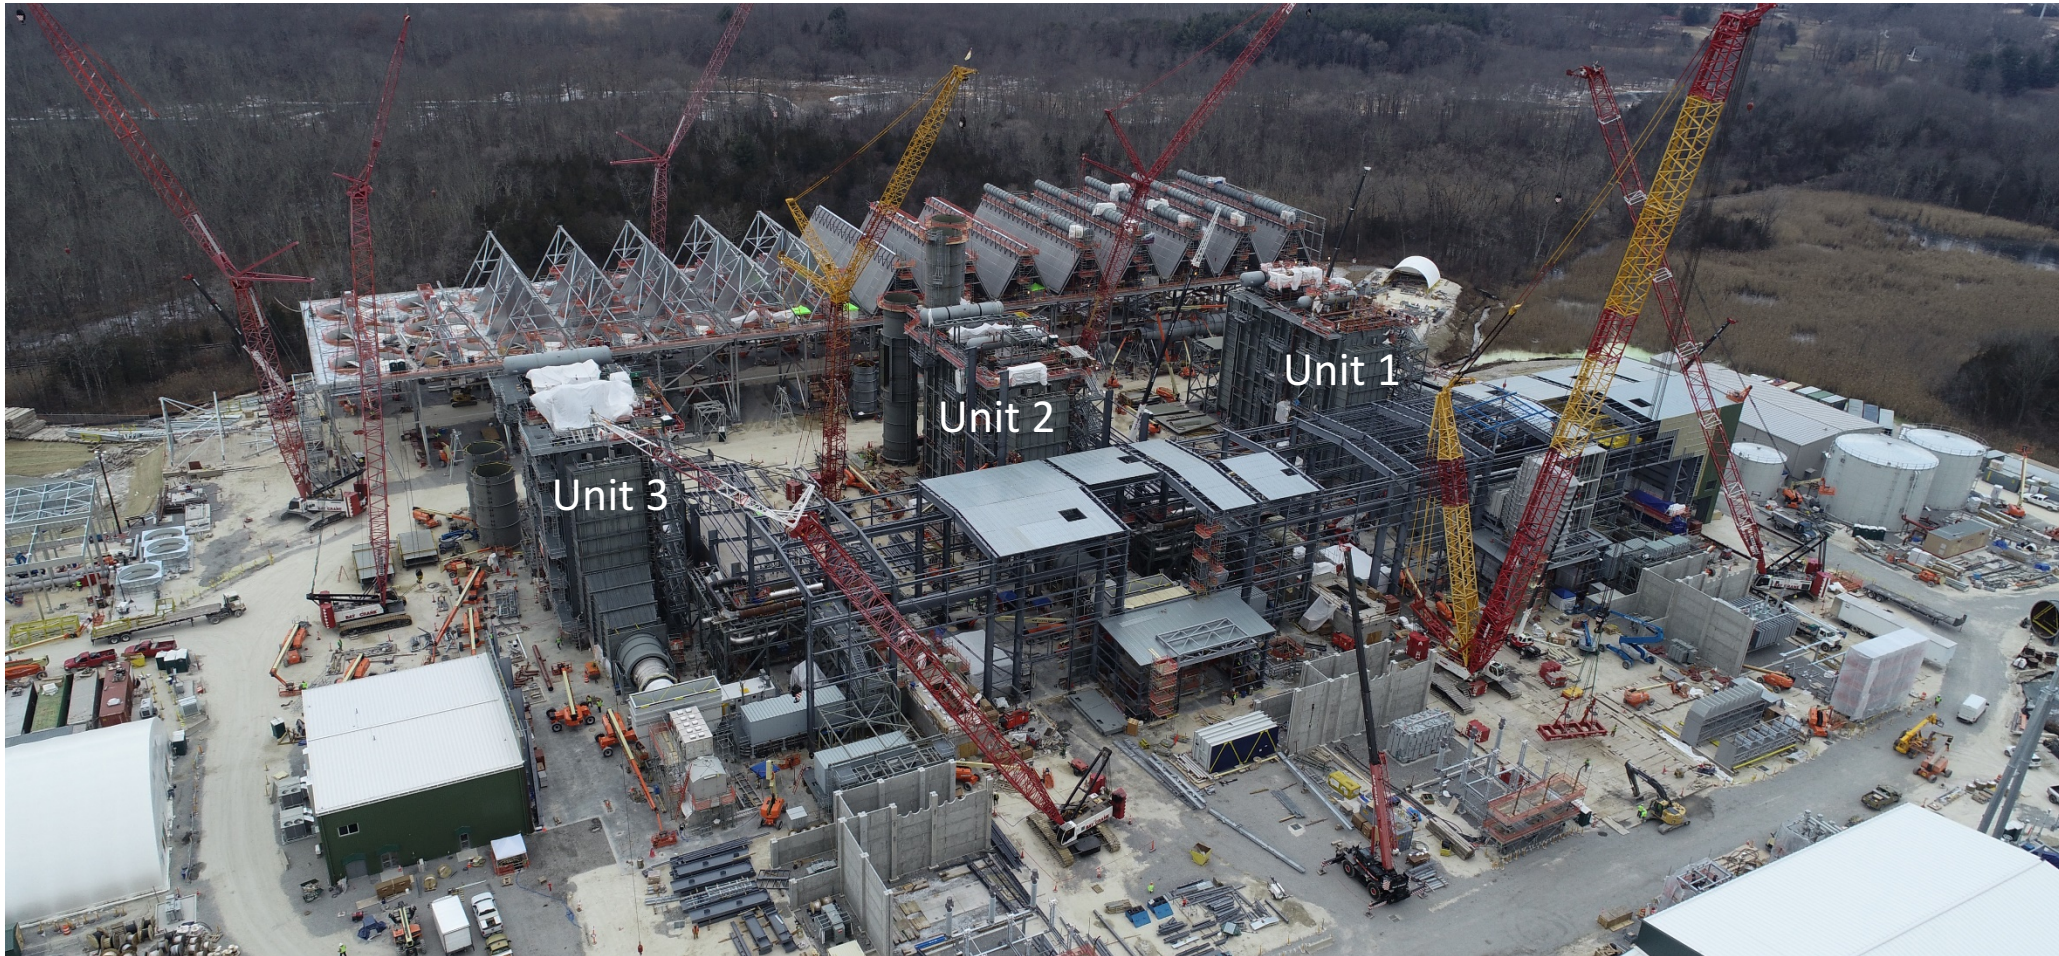

Construction Progress – Buildings Update



Looking South:

- GIS Building
- Turbine Hall
- Water Treatment Plant
- Stacks



Construction Progress – Buildings Update



Looking North:


- ACC Fan Deck
- Fin Fan
- Stack Staging Area
- Admin Building



Construction Progress - Laydown Yard



Deliveries to the Laydown Yard are now declining while deliveries from the yard to the Main Site are increasing to provide the materials needed to support construction.

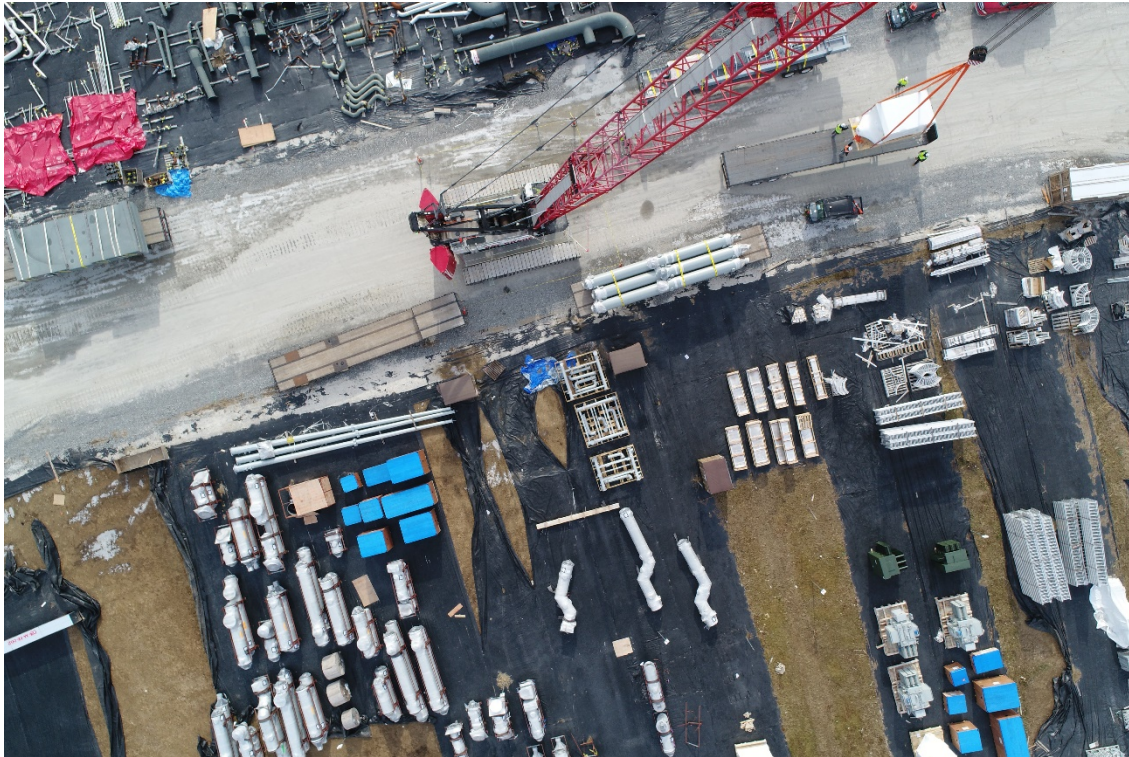

Jobs for 1,100

950+ craft workers, 18 active 1st and 2nd tier subcontractors were onsite today.



- Babcock & Wilcox - Barberton, OH
- E-J/Perreca Electric – Newburgh, NY
- Tectonic Engineering & Surveying – Newburgh, NY
- Dutchess County Constructors – Dover Plains, NY
- O&G Industries – Torrington, CT
- Empire Layout – Somers, NY
- Tri-Valley Iron – Palisades, NY
- ABB – Raleigh, NC
- LeChase Construction – Rochester, NY
- Frank Lill & Son – Rochester, NY
- Bay Crane – Hillside, NJ
- FPI Mechanical – Albany, NY
- Enerfab – Cincinnati, OH
- Oradell – Roseland, NJ
- GE – NY and CT
- RCMT – Shelton, CT
- Minimax – New Orleans, LA
- Hyundai – Fort Lee, NJ



Construction Progress Transmission Upgrade



Transmission Line Progress Update



- ✓ Continued with Tower Erection:
63 of 64 are complete
- ✓ Completed Pulling Conductor
- ✓ Completed FAA Lighting and Marker Balls



Marker Balls near Sky Acres Airport

4 Week Look Ahead – Transmission Upgrade



Activities for February/March

February

- ✓ Complete Tower Erection

March

- ✓ Complete all Line Work
- ✓ Start Restoration



Installing Conductors



Grounding Tower



Installing Conductors

Next Up



- More Information?
 - Scott Curry, Project Director
 - scurry@cricketvalley.com
