

# Monthly Progress Update

November 2018

Jobs for

**1,100**

workers



Energy for

**1,000,000**

homes



# Steps for Safety



## Safety Statistics (Job to Date)

	Generation Station	Transmission Line
Near Misses	42	5
First Aids	89	6
Recordables	7	0
Lost Time	0	0
Hours Worked	1,261,152	135,132

# Cricket Valley Energy Center Construction Progress





# Educational Outreach at Dover High School



The CVEC team helped organize a Career Fair. We gathered participants from several of our disciplines, the military and other local businesses to showcase career and employment opportunities. The students also learned what education and training are needed for success.





# Community Outreach



CVEC team members purchased Thanksgiving meals for 8 local families. They also donated items that were needed by the Center of Compassion's annual effort to deliver Thanksgiving meals throughout the community.





# Construction Highlights



On November 7, 2018, the project marked the “Million Man-Hour” Milestone with a lunch for the 850+ Craft. The time together also provided the opportunity to honor the 100+ veterans who work on site. Site Manager Jim Frank, assembled them all to receive our recognition and thanks, to take a group photo, and to receive a gift.






# Construction Progress Highlights



Exterior construction of the Admin and GIS Building are complete. Interior construction has begun as well as construction of the Water Treatment Plant.

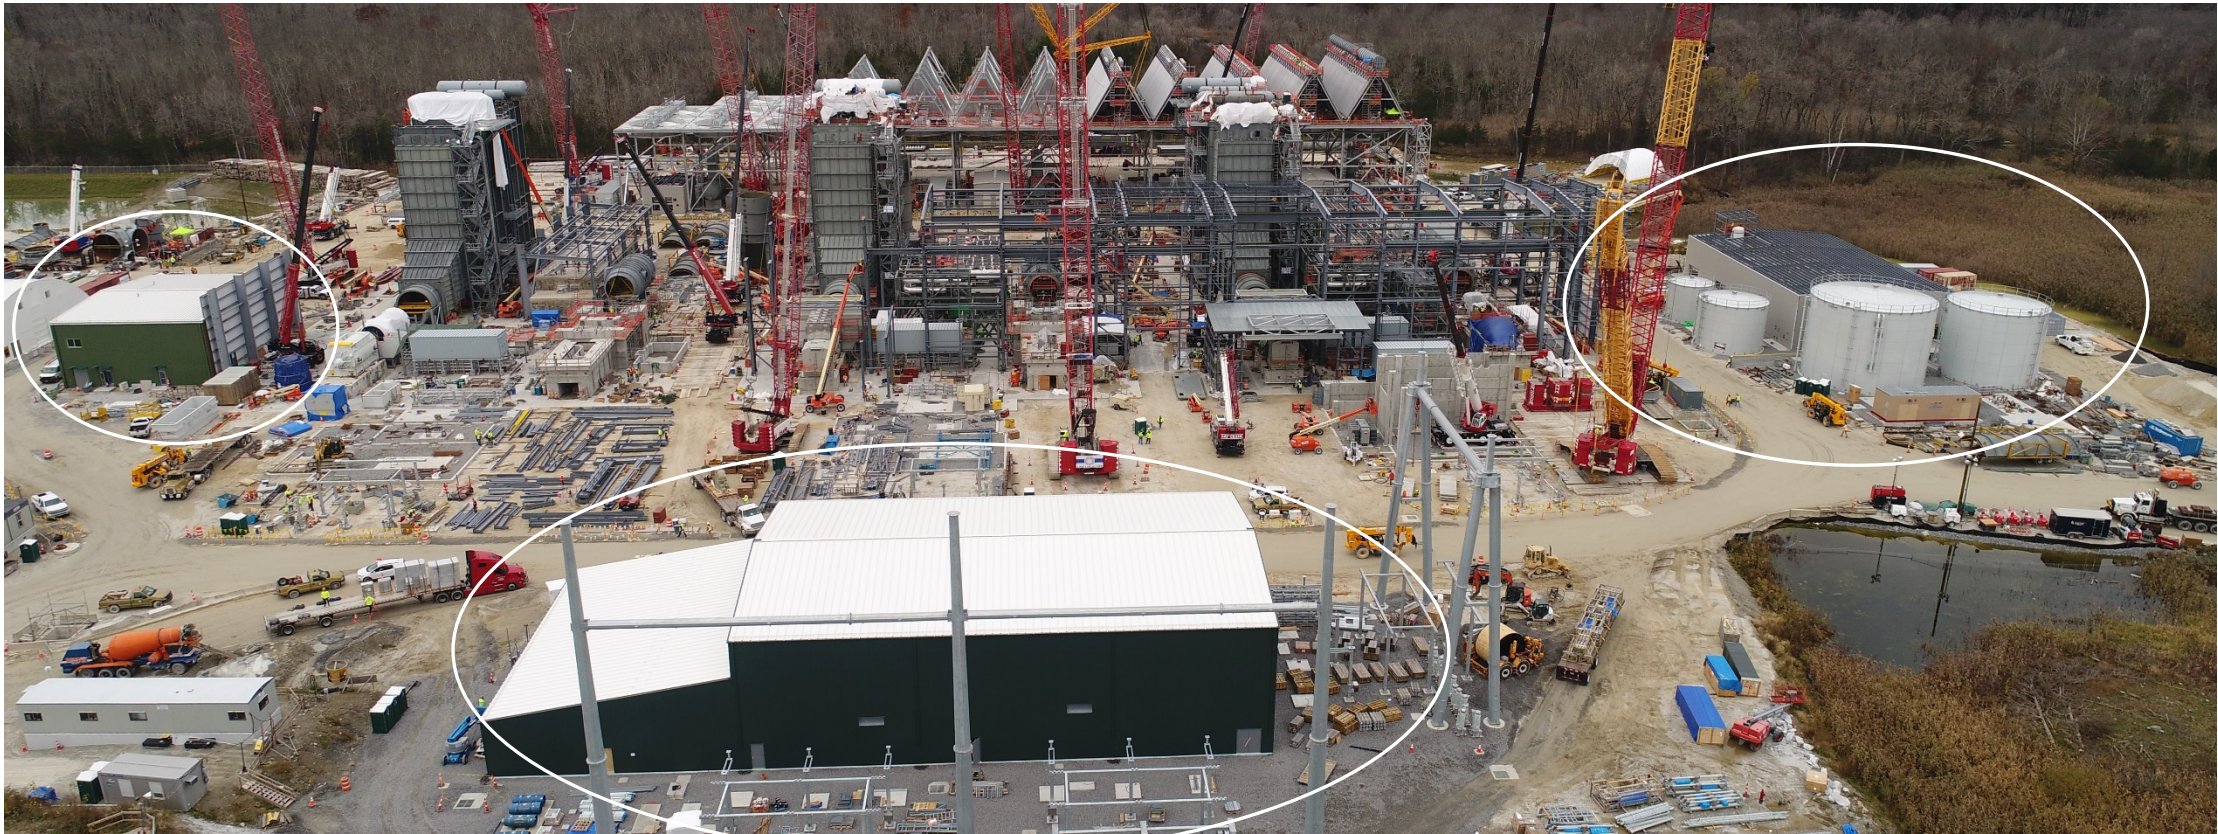



# Construction Progress Highlights



Unit 1 Steam  
Turbines are set.





# Jobs for 1,100

800+ craft workers, 17 active 1<sup>st</sup> and 2<sup>nd</sup> tier subcontractors are onsite today.



- Babcock & Wilcox - Barberton, OH
- E-J/Perreca Electric – Newburgh, NY
- Tectonic Engineering & Surveying – Newburgh, NY
- Dutchess County Constructors – Dover Plains, NY
- O&G Industries – Torrington, CT
- Empire Layout – Somers, NY
- Tri-Valley Iron – Palisades, NY
- ABB – Raleigh, NC
- LeChase Construction – Rochester, NY
- Frank Lill & Son – Rochester, NY
- Bay Crane – Hillside, NJ
- FPI Mechanical – Albany, NY
- Enerfab – Cincinnati, OH
- Oradell – Roseland, NJ
- GE – NY and CT





# Construction Progress Transmission Upgrade






# Transmission Line Progress Update



- ✓ Continued with Tower Erection  
(58 of 64 complete)
- ✓ Continued pulling conductor - Completed first pull
  - ✓ Completed dead-ending
  - ✓ Completed sagging and clipping of conductor
- ✓ Commenced setup of second pull

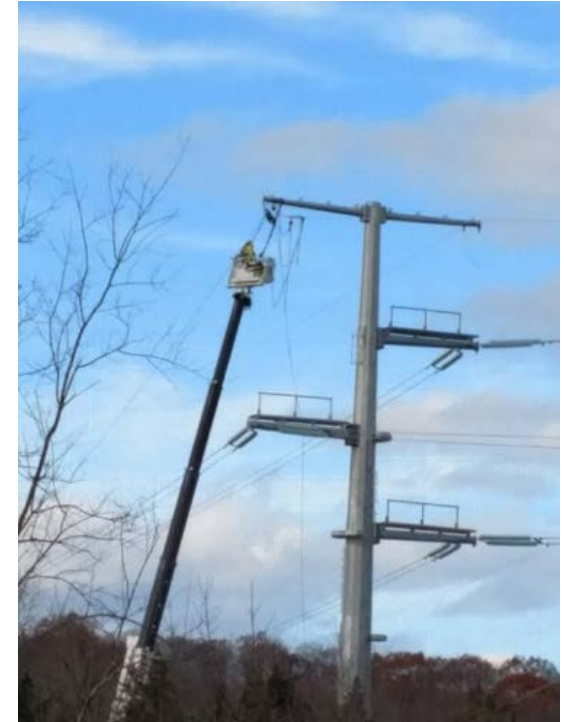

Line Work in Pleasant Valley



# 4 Week Look Ahead – Transmission Upgrade



## Activities for December

- ✓ Complete Tower Erection
- ✓ Continue Line Stringing
  - ✓ Starting at Pleasant Valley
  - ✓ Working East
  - ✓ Utilize light duty helicopters
  - ✓ Completion Mid January
- ✓ Danger Tree Removal



Installing spacers between conductors

# Active Sub-Contractors – Transmission Upgrade



- Real Time Engineering – Structure Design
- Supreme – Tree clearing, access road improvements, and work pad construction



Above: Rope Pulling Machines  
Left: Hard Line  
Center: Conductor  
Right: Straw Line



# Next Up

---



- More Information?
  - Scott Curry, Project Director
  - [scurry@cricketvalley.com](mailto:scurry@cricketvalley.com)
